

**WEEKLY UPDATE FOR
TRIAD BAPTIST CHURCH - PHASE II - WORSHIP CENTER AND CLASSROOM ADDITION
PROJECT # PS0113032
2/28/2014**

Project Status:

1. Interior Enterprises is installing ceiling grid and finishing sheet rock.
2. Varner Electric is installing lights and has the temporary permanent power inspection signed off.
3. K S & K Masonry is laying brick and split face block at the west elevation.
4. Empire Painting is painting interior walls and door frames.
5. Sentry Fire Protection is installing sprinkler head drops.
6. Systems Contractors is installing HVAC diffusers and grilles.
7. Preferred Service has installed the stained/polished concrete samples.
8. Gallimore Exterior is installing EIFS at the east elevation.

Project Photos



Southwest building corner



South elevation




North elevation



Media Center 112



Ceiling grid installation in the gym

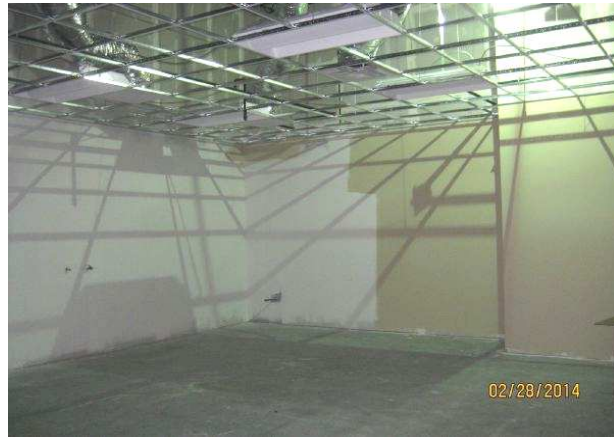

Classroom/Lab 215



Lobby 200



Classroom 211

Two-Week Schedule:

1. Interior Enterprizes to install all ceiling tile except around the basketball goals by 3/10/14.
2. Sentry Fire Protection to complete sprinkler head drops by 2/28/14.
3. Bonitz Flooring Group to install ceramic wall tile by 3/13/14.
4. Shaffer Cabinet Works to install wood trim in the gym by 3/4/14.
5. Michael Elks Co. to install basketball goals and the gym curtain by 3/14/14.
6. Gallimore Exteriors to complete EIFS by 3/12/14.
7. Allied Roofing to install standing seam metal roof by 3/12/14.
8. Bonitz Flooring Group to start installing quarry tile in the kitchen by 3/11/14.
9. Interiors Enterprizes to complete ceiling grid and tile around the basketball goals by 3/19/14.
